

First-pass yield


96.2%

Unplanned downtime


7.4 h

Body Narrative · First-pass yield improved from 94.6% to 96.2% after the valve service. Downtime remains 7.4 hours, above the 6-hour limit. Sample 19 is outside the SPC centerline pattern but inside the product specification; treat this as a process signal for investigation, not a customer defect or capability claim.


Critical measurement trend

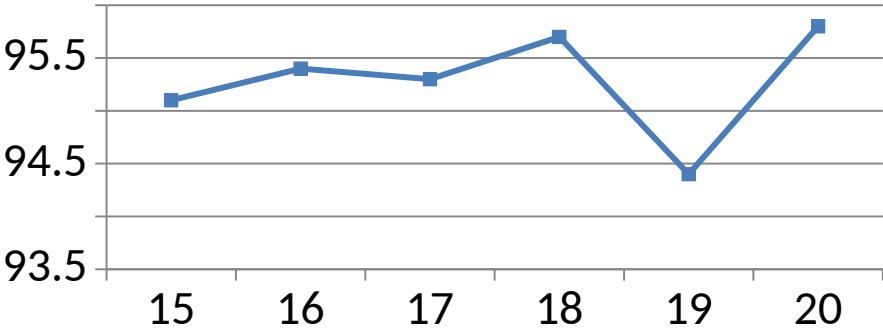

Yield by shift

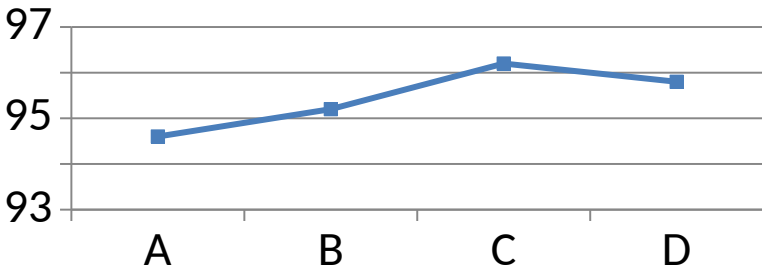

Process Flow



Area / identifier	Status	Owner	Due	Evidence
ETCH-08-A / PM-44719	Calibration open	Equipment Eng.	09-25	Pressure offset +2.4 kPa
Line 4 / sample 20	Matched rerun	Process Eng.	09-25	SPC sequence 15–20
Batch L4-260918-B-7742	Release gated	Quality	09-26	Await sign-off; no capability claim

Evidence Card

Measurement system remains within the qualified reference range.
Sample: 30 parts · method: inline metrology · source: shift B inspection.
Verified

Risk Callout · **Keep Friday capacity release conditional**
Await pressure calibration, matched sample 20, and Quality sign-off. A point inside specifications can still warrant a control-chart investigation.
· **Review**

Project Card

Complete chamber verification and update the runbook.
Owner: Equipment Engineering · due next shift · evidence: paired control lot.
Active
